

ID	Task Name	Duration	Start	Finish	Qtr 2, 2026			Qtr 3, 2026			Qtr 4, 2026			Qtr 1, 2027			Qtr 2, 2027			Qtr 3, 2027			Qtr 4, 2027	
					Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
1	CONSTRUCTION OF SOUTH ATLANTIC LNG PLANT	480 days	Mon 1 Jun '26	Thu 23 Sep '27																				
2	ENGINEERING	187 days	Mon 1 Jun '26	Fri 4 Dec '26																				
3	ISSUE FOR REVIEW ENGINEERING DELIVERABLES (FEED)	30 days	Mon 1 Jun '26	Tue 30 Jun '26																				
4	PROCESS DELIVERABLES	30 days	Mon 1 Jun '26	Tue 30 Jun '26																				
12	INSTRUMENT DELIVERABLES	30 days	Mon 1 Jun '26	Tue 30 Jun '26																				
16	ELECTRICAL DELIVERABLES	30 days	Mon 1 Jun '26	Tue 30 Jun '26																				
19	MECHANICAL DELIVERABLES	30 days	Mon 1 Jun '26	Tue 30 Jun '26																				
21	PIPING DELIVERABLES	30 days	Mon 1 Jun '26	Tue 30 Jun '26																				
25	CLIENT IFC REVIEW & APPROVAL TIMELINE ALLOCATION	10 days	Wed 1 Jul '26	Fri 10 Jul '26																				
26	HAZID STUDY MEETING	2 days	Sat 11 Jul '26	Sun 12 Jul '26																				
27	ISSUE FOR REVIEW ENGINEERING DOCUMENT (30% DED)	30 days	Mon 13 Jul '26	Tue 11 Aug '26																				
28	PROCESS DELIVERABLES	30 days	Mon 13 Jul '26	Tue 11 Aug '26																				
36	INSTRUMENT DELIVERABLES	30 days	Mon 13 Jul '26	Tue 11 Aug '26																				
44	ELECTRICAL DELIVERABLES	30 days	Mon 13 Jul '26	Tue 11 Aug '26																				
60	TECHNICAL SAFETY DELIVERABLES	30 days	Mon 13 Jul '26	Tue 11 Aug '26																				
63	MECHANICAL DELIVERABLES	30 days	Mon 13 Jul '26	Tue 11 Aug '26																				
67	PIPING DELIVERABLES	30 days	Mon 13 Jul '26	Tue 11 Aug '26																				
71	CLIENT IFC REVIEW & APPROVAL TIMELINE ALLOCATION	14 days	Wed 12 Aug '26	Tue 25 Aug '26																				
72	PROJECT HAZOP STUDY MEETING	10 days	Wed 26 Aug '26	Fri 4 Sep '26																				
73	ISSUE FOR CONSTRUCTION ENGINEERING DOCUMENT (100% DED)	45 days	Sat 5 Sep '26	Mon 19 Oct '26																				
74	PROCESS DELIVERABLES	45 days	Sat 5 Sep '26	Mon 19 Oct '26																				
84	INSTRUMENT DELIVERABLES	45 days	Sat 5 Sep '26	Mon 19 Oct '26																				
96	ELECTRICAL DELIVERABLES	45 days	Sat 5 Sep '26	Mon 19 Oct '26																				
115	TECHNICAL SAFETY DELIVERABLES	45 days	Sat 5 Sep '26	Mon 19 Oct '26																				
118	MECHANICAL DELIVERABLES	45 days	Sat 5 Sep '26	Mon 19 Oct '26																				
124	PIPING DELIVERABLES	45 days	Sat 5 Sep '26	Mon 19 Oct '26																				
131	CIVIL DELIVERABLES	45 days	Sat 5 Sep '26	Mon 19 Oct '26																				
137	PROJECT MANAGEMENT DELIVERABLES	45 days	Sat 5 Sep '26	Mon 19 Oct '26																				
145	CLIENT IFC REVIEW & APPROVAL TIMELINE ALLOCATION	21 days	Tue 20 Oct '26	Mon 9 Nov '26																				
146	PROCUREMENT	265 days	Tue 10 Nov '26	Sun 1 Aug '27																				
147	MANUFACTURING OF LNG EQUIPMENT	150 days	Tue 10 Nov '26	Thu 8 Apr '27																				
148	FEED GAS FILTERING AND METERING UNIT	150 days	Tue 10 Nov '26	Thu 8 Apr '27																				
150	ACID REMOVAL UNIT	150 days	Tue 10 Nov '26	Thu 8 Apr '27																				
152	DEHYDRATION UNIT	150 days	Tue 10 Nov '26	Thu 8 Apr '27																				
155	LIQUEFACTION UNIT	150 days	Tue 10 Nov '26	Thu 8 Apr '27																				
158	REFRIGERANT COMPRESSION	150 days	Tue 10 Nov '26	Thu 8 Apr '27																				
161	REFRIGERANT MAKE-UP UNIT	150 days	Tue 10 Nov '26	Thu 8 Apr '27																				
164	LNG STORAGE AND LOADING	150 days	Tue 10 Nov '26	Thu 8 Apr '27																				
166	BOG RECOVERY UNIT	150 days	Tue 10 Nov '26	Thu 8 Apr '27																				
168	UTILITIES	150 days	Tue 10 Nov '26	Thu 8 Apr '27																				
171	TESTING / INSPECTION EQUIPMENT	10 days	Fri 9 Apr '27	Sun 18 Apr '27																				
172	SHIPPING OF EQUIPMENT	60 days	Mon 19 Apr '27	Thu 17 Jun '27																				
173	CUSTOM CLEARANCE AND ARRIVAL OF EQUIPMENT TO INSTALLATION YARD	15 days	Fri 18 Jun '27	Fri 2 Jul '27																				
174	CIVIL CONSTRUCTION	107 days	Mon 19 Apr '27	Tue 3 Aug '27																				
175	CIVIL EQUIPMENT FOUNDATION	40 days	Mon 19 Apr '27	Fri 28 May '27																				
176	UTILITIES FOUNDATION	35 days	Mon 19 Apr '27	Sun 23 May '27																				
178	EQUIPMENT FOUNDATION	40 days	Mon 19 Apr '27	Fri 28 May '27																				

Project: SOUTH ATLANTIC 5MM

Date: Thu 30 Apr '26

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

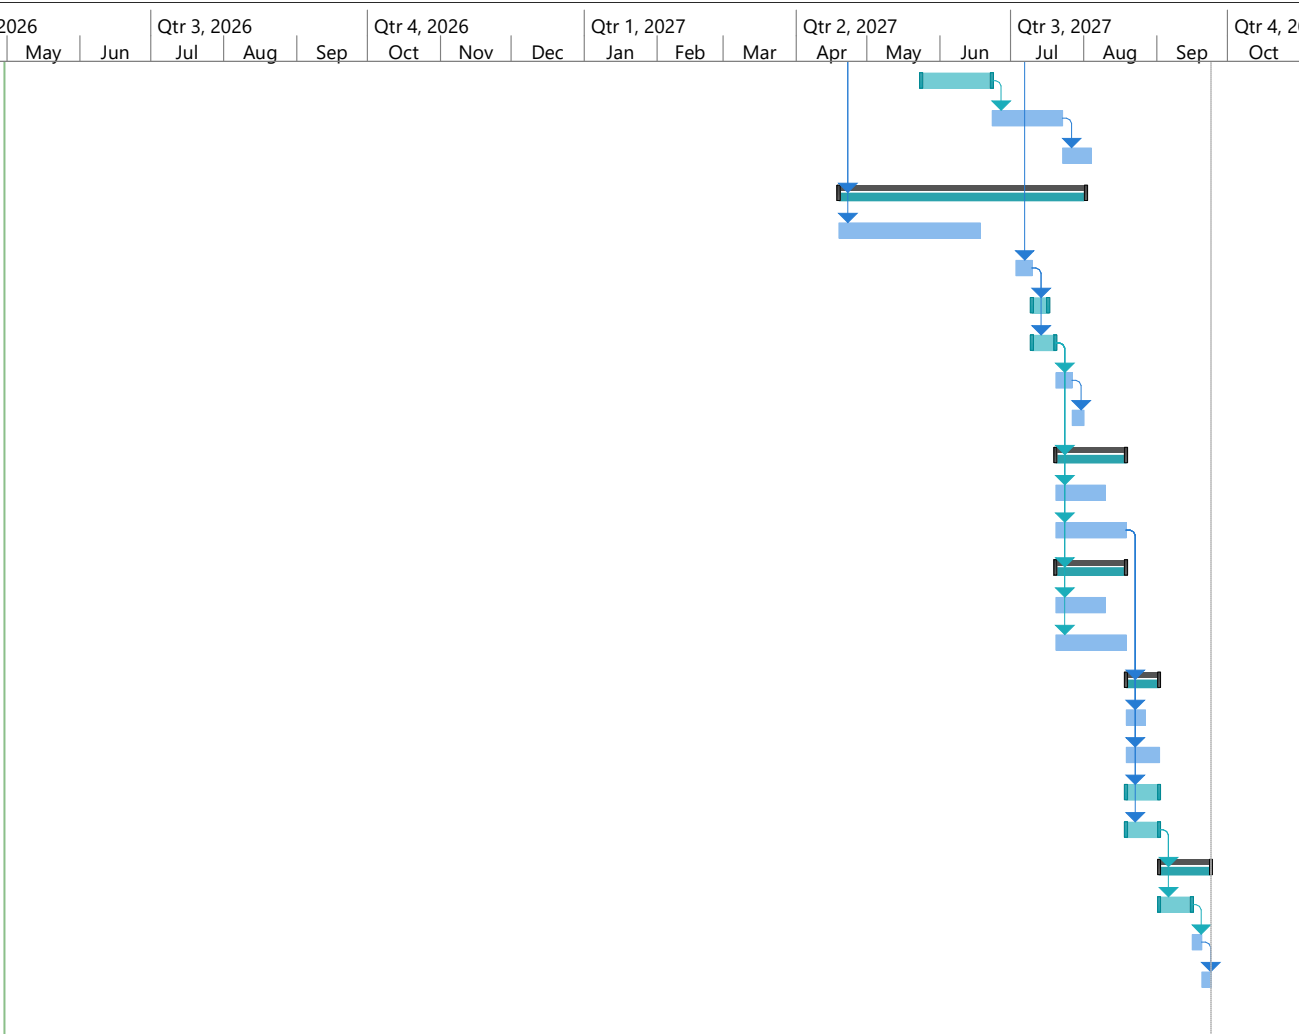
External Milestone

Deadline

Progress

Manual Progress

Page 1

ID	Task Name	Duration	Start	Finish	Qtr 2, 2026			Qtr 3, 2026			Qtr 4, 2026			Qtr 1, 2027			Qtr 2, 2027			Qtr 3, 2027			Qtr 4, 2027	
					Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
180	TANK FARM, PIPE RACK AND LOADING BAY	30 days	Mon 24 May '27	Tue 22 Jun '27																				
181	INTERNAL ROAD & DRAINAGE NETWORK	30 days	Wed 23 Jun '27	Thu 22 Jul '27																				
182	LANDSCAPING	12 days	Fri 23 Jul '27	Tue 3 Aug '27																				
183	MECHANICAL & PIPING INSTALLATION	105 days	Mon 19 Apr '27	Sun 1 Aug '27																				
184	FABRICATION OF OFFSKID PIPING	60 days	Mon 19 Apr '27	Thu 17 Jun '27																				
185	MECHANICAL ERECTION	7 days	Sat 3 Jul '27	Fri 9 Jul '27																				
186	PIPE RACK INSTALLATION	7 days	Sat 10 Jul '27	Fri 16 Jul '27																				
187	OFFSKID PIPING INSTALATION	10 days	Sat 10 Jul '27	Mon 19 Jul '27																				
188	HYDROTESTING	7 days	Tue 20 Jul '27	Mon 26 Jul '27																				
189	PAINTING	5 days	Tue 27 Jul '27	Sat 31 Jul '27																				
190	ELECTRICAL INSTALLATION	30 days	Tue 20 Jul '27	Wed 18 Aug '27																				
191	ELETRICAL CABLE PULLING	21 days	Tue 20 Jul '27	Mon 9 Aug '27																				
192	ELECTRICAL DEVICES INSTALLATION	30 days	Tue 20 Jul '27	Wed 18 Aug '27																				
193	INSTRUMENT INSTALLATION	30 days	Tue 20 Jul '27	Wed 18 Aug '27																				
194	INSTRUMENT CABLE PULLING	21 days	Tue 20 Jul '27	Mon 9 Aug '27																				
195	INSTRUMENT DEVICE INSTALLATION	30 days	Tue 20 Jul '27	Wed 18 Aug '27																				
196	PLANT PRECOMMISSIONING	14 days	Thu 19 Aug '27	Wed 1 Sep '27																				
197	AIR BLOWING & N2 PURGING	8 days	Thu 19 Aug '27	Thu 26 Aug '27																				
198	PLANT UTILITES PRECHECK & START-UP	14 days	Thu 19 Aug '27	Wed 1 Sep '27																				
199	HOT AND COLD LOOP TEST	14 days	Thu 19 Aug '27	Wed 1 Sep '27																				
200	SOFTWARE INTEGRATION	14 days	Thu 19 Aug '27	Wed 1 Sep '27																				
201	PLANT COMMISSIONING	22 days	Thu 2 Sep '27	Thu 23 Sep '27																				
202	INTRODUCTION OF HYDROCARBON INTO SOUTH ATLANTIC LNG PLANT	14 days	Thu 2 Sep '27	Wed 15 Sep '27																				
203	OFFTAKING OF LNG	4 days	Thu 16 Sep '27	Sun 19 Sep '27																				
204	OFFTAKING OF NGL	4 days	Mon 20 Sep '27	Thu 23 Sep '27																				
205																								

Project: SOUTH ATLANTIC 5MM Date: Thu 30 Apr '26	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
