

**TECHNICAL ADVISORY SERVICE
5MMSCFD MINI-LNG PLANT**


SOUTH ATLANTIC LNG WEST AFRICA LIMITED

SERVICE PROPOSAL

Proposal valid until 31.05.2026

06.02.2026 20877-ILF-NGR-OD-00001 | Revision 0

© ILF

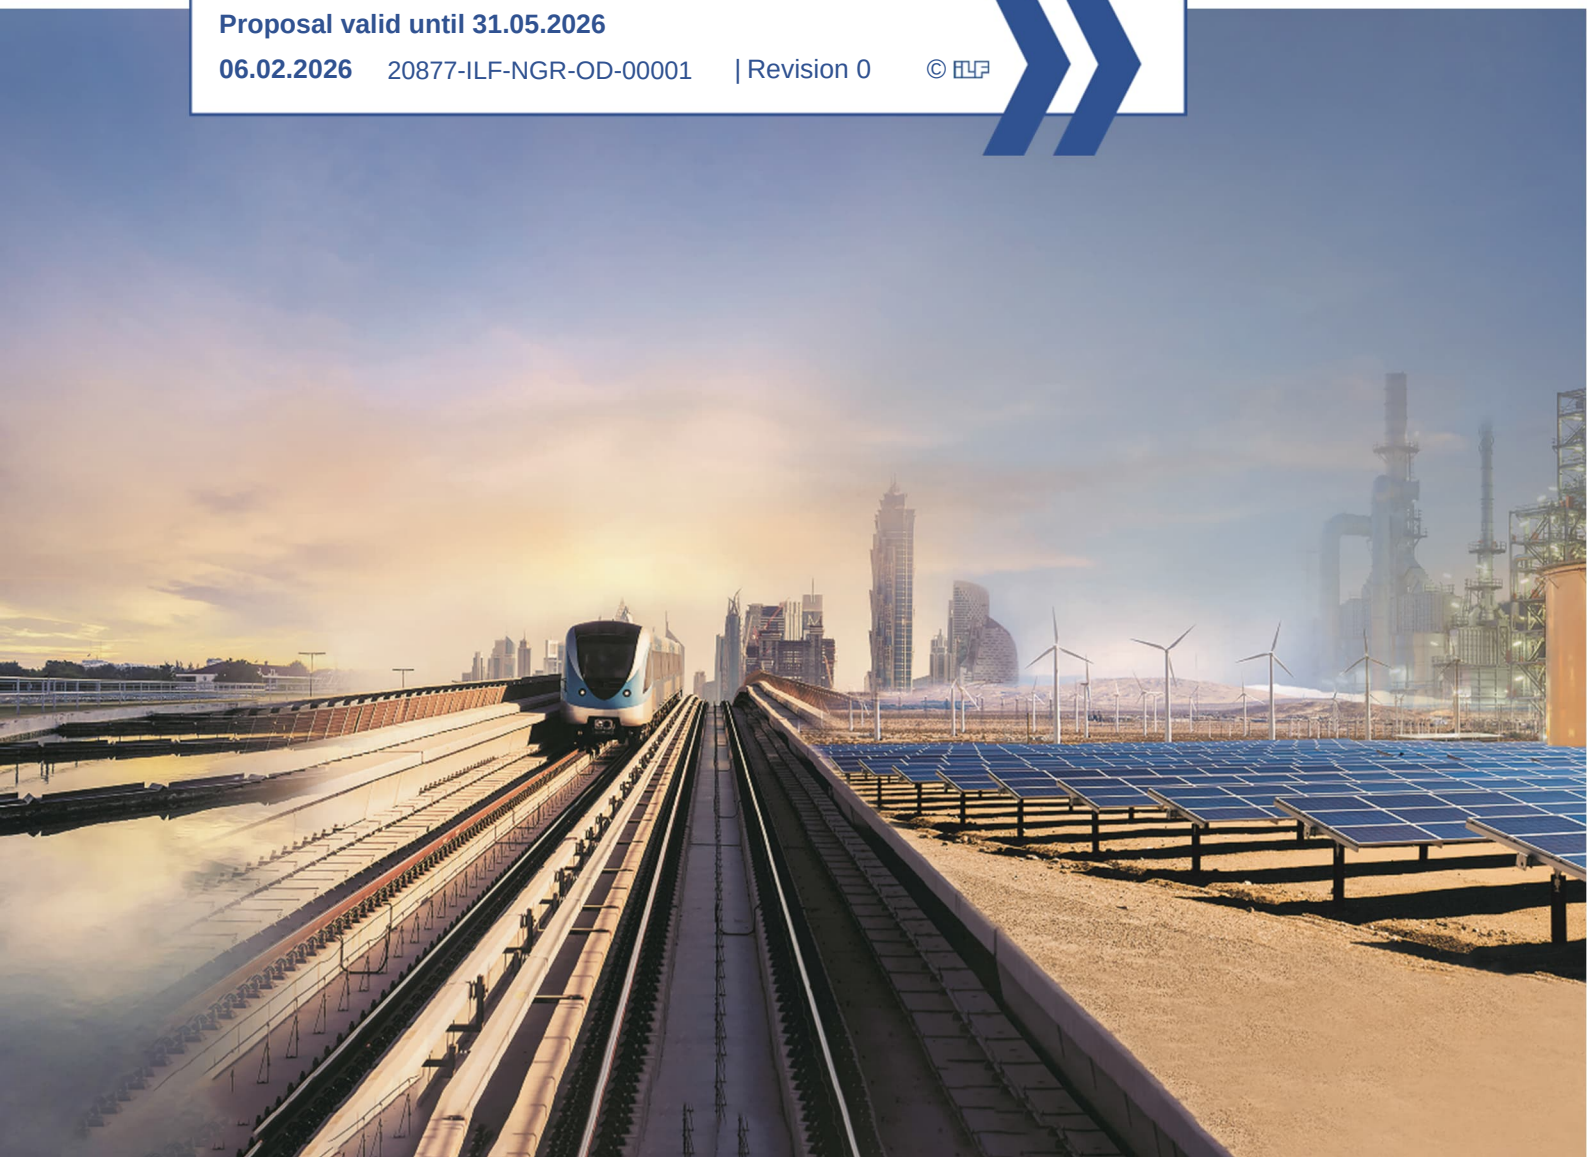

REVISION

0	09.03.2026	Issued for use	N. Nworgu	M. Olaleye	A. Oshodi
REV.	DATE	PURPOSE	PREPARED	CHECKED	APPROVED

YOUR POINT OF CONTACT WITHIN ILF



ABIODUN OSHODI

ILF Engineers Nigeria Ltd.

TCF Tower, 33 Adeola Hopewell Street

Victoria Island, Lagos, Nigeria

Tel.: +234 / (0) 1 453 7015/ 7016

mailto: Abiodun.Oshodi@ilf.com

www.ilf.com

TABLE OF CONTENTS

1	INTRODUCTION.....	6
1.1	Background.....	6
1.2	Request for Proposal.....	6
1.3	Purpose of this document.....	6
1.4	Validity of Offer.....	6
1.5	Objective of the proposed service	7
2	GROUP PROFILE & PHILOSOPHY	8
3	WORKING EXPERIENCE IN THE REGION	11
3.1	References.....	14
4	SCOPE OF SERVICE	15
4.1	General Outline	15
5	ILF’S APPROACH	16
6	METHODOLOGY.....	17
6.1	Proposed Methodology and Work Plan	17
6.2	EPC Contract	18
6.3	Engineering Design Review	19
6.4	Procurement Supervision	20
6.5	Construction Monitoring	20
6.6	Close-out Report.....	22
6.7	Location	23
6.8	Key Resources.....	24
6.9	Safety on Site.....	27
7	COMMERCIAL PROPOSAL.....	28
7.1	Labour Cost	28
7.2	Non Labour Costs	28
7.3	Payment Schedule	29
7.4	Reimbursable Rates.....	30
7.5	Non Labour Costs	31
8	ASSUMPTIONS AND EXCLUSIONS	32
8.1	Exclusions from Services	33
9	CONTRACT	34
9.1	Contractual Liability Cap	34
9.2	Project Language	34

9.3	Exclusion of Consequential Damages	34
10	CONCLUSION	35
11	ATTACHMENTS.....	36

LIST OF TABLES

Table 1: Project References	11
Table 2 – Key resource	24
Table 3: Payment Schedule	29
Table 4: Reimbursable Rate	30

FIGURES

Figure 1 - ILF offices worldwide.....	8
<i>Figure 2: Technical Advisory Services.</i>	<i>17</i>
<i>Figure 3:Preliminary Execution Strategy</i>	<i>25</i>
<i>Figure 4: Manning Chart.</i>	<i>26</i>



1 INTRODUCTION

1.1 Background

South Atlantic LNG West Africa Limited (“the Client” or “SA LNG”) is an indigenous company located in Lagos Nigeria with specialized skills providing ancillary services to the power and oil & gas sectors in Nigeria.

The client is proposing to build a 5MMSCFD Mini-LNG Plant in Ibefun axis and have received a firm offer from a Chinese EPC contractor for the FEED, Detailed Engineering, Procurement and Fabrication, Construction and Installation works. Client's proposed timeline is 16 months.

Client has also secured equity financing from the Midstream and Downstream Gas Infrastructure Fund (MDGIF).

1.2 Request for Proposal

The Client has asked ILF (the Consultant) to provide “Project Management and Consultancy Services - PMC” service for the development / construction of a 5MMSCFD Mini-LNG Plant in the Ibefun area (the project).

In further conversation with the Client and in consideration of client's budget, ILF is proposing to offer “Technical Advisory – TA” for the EPCI for the 5MMSCD Mini-LNG Plant (“Project”).

1.3 Purpose of this document

This document is ILF's proposal demonstrating ILF's capabilities, scope of service, consultant's experience, execution methodology and available key resources to provide services for the project.

1.4 Validity of Offer

Our proposal is valid for One Hundred and Eighty (180) days from the date of this proposal.



1.5 Objective of the proposed service

The services detailed in this proposal will achieve the following;

- **Safety:** Ensure the safety of the facility's function and that project execution methodology is environmentally acceptable and considers human factors in its implementation.
- **Cost Efficiency:** ILF will ensure that its service will support efficient utilization of budget cap for project development.
- **Certified Design Standards:** ILF's services will meet the most stringent Nigerian regulatory standard, COMPANY guide, practices & specifications and industry odes & Standards.
- **Compliance with Standards:** ILF's works are consistent with operational reliability and safety philosophy.

2 GROUP PROFILE & PHILOSOPHY

ILF is a leading independent international multi-disciplinary engineering and consulting company offering a broad range of services on major industrial and infrastructural projects worldwide **for over 55 years**. With over 2,500 highly qualified employees in more than **45 office locations** across five continents, the companies of ILF have a strong global presence. ILF combines excellent consulting expertise and a broad international background with project-specific expertise and an in-depth understanding of local requirements due to a stable, long-established presence in its markets. It is completely independent with no affiliation to construction firms, suppliers or financial institutions. Objectivity through independence is a key aspect of its business philosophy.

ILF management procedures are ISO 9001, 14001 and OHSAS 18001 certified.



“ILF combines local presence and international expertise to best serve clients’ needs.”

Klaus Lässer, CEO




Figure 1 - ILF offices worldwide

ILF has executed more than 9,500 projects successfully in over 150 countries. The company has over 55 years of experience in the energy and oil and gas sectors worldwide, by providing comprehensive services for major industrial and infrastructure projects in the following business areas:

- Energy & Climate Protection

- Water & Environment
- Transportation & Urban Spaces
- Oil, Gas & Industrial

ILF primarily employs consulting engineers with expertise in electrical, civil, mechanical, process, instrumentation and economic engineering/business administration who are capable of providing a wide range of engineering, project management and consultancy services through all project development phases from early conceptual and feasibility studies, including Master Plans, through planning and design to construction and commissioning and ultimately operations.

Across its offices, ILF has staff in a large variety of other disciplines, such as business administration, geology, environment protection, chemistry and many others. Apart from technical scope, many projects typically have significant commercial, economic and regulatory aspects that need to be addressed by customizing project services. ILF Group offers a comprehensive set of services for the energy industries related to project finance, merger & acquisition, project management and capacity building.

In more detail the ILF's Services comprise:

- feasibility studies for power and oil & gas facilities, such as power plants, processing facilities (including petrochemical), pipelines, loading facilities and other relevant installations
- sound cost estimates for oil & gas facilities based on 50 years of project experience
- physical planning of infrastructure installations, FEED and the following detailed design, and management of the development and commissioning of the new facilities
- the setup of management and operational systems to the point that the new facility becomes an independent functional entity
- comprehensive risk assessments addressing process safety as well as occupational health & safety and environment, and development of emergency response plans
- supporting vendors and investors during the divestiture / acquisition phase by assessing the value, inherent strengths and associated risks of the assets in question
- assignments as lender's engineers where our experts estimate the construction budget and schedule from an independent perspective and check whether

borrower's assumptions are reasonable and include the proper level of contingencies

- due diligences developing detailed operational and business plans as well as comprehensive financial models serving as base case model for project finance
- carrying out workshop and in-house training, e.g. on financial modeling, project management or contract and claims management

Vision, Values & Beliefs

ILF passionately devotes its energy to pursuing the vision of improving the global quality of life. This is what drives the company and makes its employees believe in their work.

It is motivated by its ambition to achieve market leadership through quality. This is why it focuses on a structured approach to problem solving and is constantly striving to improve. But above all, it is its great people that really make the difference. They truly believe in respect, honesty, reliability and fairness as a solid foundation for all our interactions.

ILF continues to spearhead Engineering Excellence. Its independence allows it to provide creative solutions while continuously acting in every client's best interest.



3 WORKING EXPERIENCE IN THE REGION

ILF is qualified and has demonstrated experience in the assignment through its broad range of project experience located in Western Africa. Our local presence in Lagos, Nigeria and in Accra, Ghana offers both local and regional expertise and is strengthened by its global reach of experts across ILF's over 45 offices worldwide. Our recent projects involving Technical Consultancy scope projects in West Africa are:

Table 1: Project References

S/No.	PROJECT DESCRIPTION	PROJECT LOCATION	PROJECT DURATION	CLIENT
01	Ajaokuta - Kaduna - Kano Gas Pipeline PMC Services	Lagos, Nigeria	Jan., 2020 - Ongoing	NNPC-Nigerian National Petroleum Corporation, Garki, Abuja
02	Engineering Design and Project Support Services (ESA)	Nigeria	June 2022 - Ongoing	Shell Petroleum Development Company of Nigeria
03	Rehabilitation of FPSO	Benin, Nigeria	June 2022 - Ongoing	NNPC Exploration and Production Limited
04	Gas Pipeline Network – Vendor Due Diligence	Nigeria	July, 2020 – July, 2021	Axxela
05	Technical Environmental Due Diligence Hydrocarbon Infrastructure	Nigeria	Nov, 2020 – Jan, 2021	Petrolex
06	Consultancy Services for the Proposed Regional Gas Transmission Pipeline from Benin Republic - Niger Republic	Cotonou, Benin Republic	Jan., - May, 2020	Benin LNG Company
07	Gbarain Power Plant - Shoreline Protection of NIPP 18" X 1.5Km Gas Pipeline	Lagos, Nigeria	Mar., 2020 - Ongoing	Niger Delta Power Holding Company Limited
08	210 MTD Mini LNG project, Nigeria, Risk Assessment	Lagos, Nigeria	Jan – May 2020	Confidential
09	10 MW Kano Solar Power Project - Consultancy Services, Energy audit and Power evacuation studies	Nigeria	2019 - 2020	NSIA
10	Technical Due Diligence on Gas Processing Plant	Lagos, Nigeria	Feb., - Mar., 2019	Africa Plus Partner
11	Sublime LPG Terminal Lekki-Nigeria, Review of Technical Pre-Feasibility Study	Lagos, Nigeria	Nov. 2017 – Nov. 2019	Xploit Nigeria Limited / Nigeria

S/No.	PROJECT DESCRIPTION	PROJECT LOCATION	PROJECT DURATION	CLIENT
12	Technical Due Diligence Study for Axxela Group Assets	Lagos, Nigeria	Feb., - Mar., 2019	Elektron Petroleum Energy and Mining Limited
13	210 MTD Mini LNG project, Nigeria, Conceptual Design and FEED	Lagos, Nigeria	June 2019 – Oct 2019	Confidential
14	Conversion of a Simple Cycle to Combined Cycle Power Plant - Lender's Advisor, Technical and Commercial Due Diligence	Ghana	Oct, 2015 – Jan 2018	Lending Bank (Confidential)
15	10 Power Plants (Gas Engine driven) 60 MW Captive Power Generation Portfolio, Tricap Nigeria – Technical Due Diligence, Feasibility Study	Nigeria	Mar – Oct, 2015	Financial Investor (Confidential)
16	Value for Money analysis – Technical, Commercial	Ghana	Mar – Oct, 2015	Plant Operator (Confidential)
17	Detailed Design of Ijora LPG Terminal	Lagos, Nigeria	April 2015 - September 2015	Gas Terminalling Global Operations Limited
18	Pre-Feasibility Study for an LPG Storage Terminal	Nigeria	May 2015 – July 2015	Hyde Energy
19	Design Review of OSPP Tank Farm and Terminal Project	Cotonou, Benin, West Africa	May 2015 - June 2015	Socar, Switzerland
20	Multi-product Pipeline from Dangote Jetty and tank terminal, LFTZ to PPMC Mosimi Depot - Concept Study	Lagos, Nigeria	Aug 2014 – Feb 2015	Dangote
21	Engineering Design Services for EHPL Early Utilization Pipeline Project	Nigeria	March, 2014 – Aug 2014	Acugas / Septa Energy
22	3 Gas Power Plants – Technical Due Diligence for Investor	Nigeria	Oct, 2013 – Jan, 2014	Quantum Power-Nigeria
23	Greater Lagos Gas Distribution Project, GNL, Consultancy Services	Nigeria	Dec., 2013 – April, 2014	Gaslink
24	Project Management Consultancy Services for a Marine Jetty, pipeline and distribution facility EPC Contract	Nigeria	May 2012 – June 2014	Oando PLC
25	Rehabilitation of an Import Berth Platform and Tank Farm facilities at Escravos	Escravos, Nigeria	April 2012 – Aug 2013	NNPC

S/No.	PROJECT DESCRIPTION	PROJECT LOCATION	PROJECT DURATION	CLIENT
26	Detailed Engineering Services of Oron Gas Pipeline	Nigeria	May, 2012 – February, 2013	Acugas / Septa Energy
27	Due Diligence study for an LPG Terminal	Nigeria	May 2012 – Oct 2012	Oando PLC
28	Project Management Services, Seme Field Re-Development Project	Seme, Republic of Benin	February, 2012 – September 2015	South Atlantic Petroleum Company
29	Owners Engineers SERVICES FOR JETTY EXECUTION	Nigeria	November 2011 - March 2013	Oando
30	Detailed Engineering Services; QIT Flare Gas Elimination Project	Nigeria	June 2011 to May 2012	Sudelettra Nigeria Limited
31	Feasibility Study and FEED - Gas Pipeline Distribution	Nigeria	June 2011 - November 2012	Oando / Gaslink
32	FEED Services - Seme Field Development – Plem & Admiralty Buoy	Seme, Republic of Benin	July 2011 – Nov. 2011	EPIC Atlantic /SAPETRO
33	Rehabilitation of New Atlas Cove to Mosimi 16” Multi-Products Pipeline Project	Nigeria	November 2010 - December 2013	Nigerian National Petroleum Corporation
34	Feasibility Study for Petroleum Products Supply & Storage Terminal in the Lekki Free Trade Zone	Lekki Free Trade Zone - Nigeria	March, 2008 – July 2008	DBN / DBN
35	Petroleum Products Delivery System from New SPM to Marketers Jetties at APAPA - FEED Engineering	APAPA - Nigeria	August 2007 – February 2008	OANDO PLC
36	Petroleum Products Terminal in the Lekki Free Trade Zone or any other Oando selected location	Lagos	August 2007 – January 2008	Oando PLC
37	Engineering Design & EIA Study for LPG Facilities	Tamora Island - Lagos	2007 – 2008	Linetrade Gas Limited
38	Revamp of ATLAS COVE Depot Facilities	Nigeria	August, 2006 – September, 2008	Pipelines and Products Marketing Company
39	Oben – Ajaokuta – Abuja – Kaduna Gas Pipeline System	Oben – Ajaokuta – Abuja – Kaduna	Nov. 2006 – March 2007	NGC / POSCO
40	Rehabilitation of Escravos IBP and Tank facilities	Escravos, Nigeria	2005 – 2006	Pipelines and Products Marketing Company

3.1 References

A process overview demonstrating ILF's capacity is given in the attachment(s) below:

Attachment 1 – Company Brochures



4 SCOPE OF SERVICE

4.1 General Outline

- The TA (Technical Advisor) shall review the projected construction programme, expenditure schedule and adequacy of the arrangements made at the site to achieve the projected construction schedule on a monthly basis;
- The TA shall review, assist, advise and report to the client on the progress of work on a monthly basis, vis-à-vis program of construction and milestone dates specified in the various construction and procurement agreements related to the development of the project;
- Engineering vetting for FEED and Detailed Design – define certain milestones for which the FEED and DED packages will be reviewed.
- Procurement Support – review of procurement packages
- The TA shall carry out spot verification of the quality of the various components of Project vis-à-vis approved specifications;
- The TA shall review quality control tests carried out;
- The TA shall review and assess variation orders;
- The TA shall review adherence to environmental regulations and report on any present / future risks that arise during Project implementation; assess compliance with HSE and environment and social management plan specified in the Facility agreement
- The TA shall bring to the notice of the client any event, which may lead to a Force Majeure event as laid down under contracts related to construction and procurements of various components of the Project, which may lead to time or cost overrun;
- The TA shall review the status of necessary approvals, permits, licenses, notifications, Project completion certificates, etc. as may be required for implementation of the Project;
- Identification and review of cost overruns (if any) and on time over runs (if any) and make recommendation.
- The TA shall from PMC's and EPC's monthly report, provide a report to the client.

5 ILF'S APPROACH

ILF's project execution strategy will be governed by the principle to minimize risks that would possibly endanger the most important targets, namely the quality of the work and the budget conformity.

ILF will follow the hereunder listed general principles which will facilitate the execution.

- ILF will assign personnel for this project on a long term basis in order to ensure continuity and synergies.
- All services will be coordinated by ILF's project management.
- ILF will use latest technology tools for design work review. This ensures transparent and easy change management and minimizes conflicts during construction.
- The technical strategy will be governed by the principle to minimize risks that would possibly endanger the quality or overrun the budget or drastically endanger the foreseen completion date. That involves a close and transparent cooperation with Client, which is in our opinion an absolute must for such a specific project.
- Technical queries will be collected and processed according to the requirements of the contract and discussed and agreed with Client. It is an ILF policy to treat this matter fully transparent to the Client and to agree in close co-operation on the best economical and technical solution.

6 METHODOLOGY

6.1 Proposed Methodology and Work Plan

The main contents of the Lender's Technical Consultant either in an integrated team or as an independent consultant shall include as a minimum:

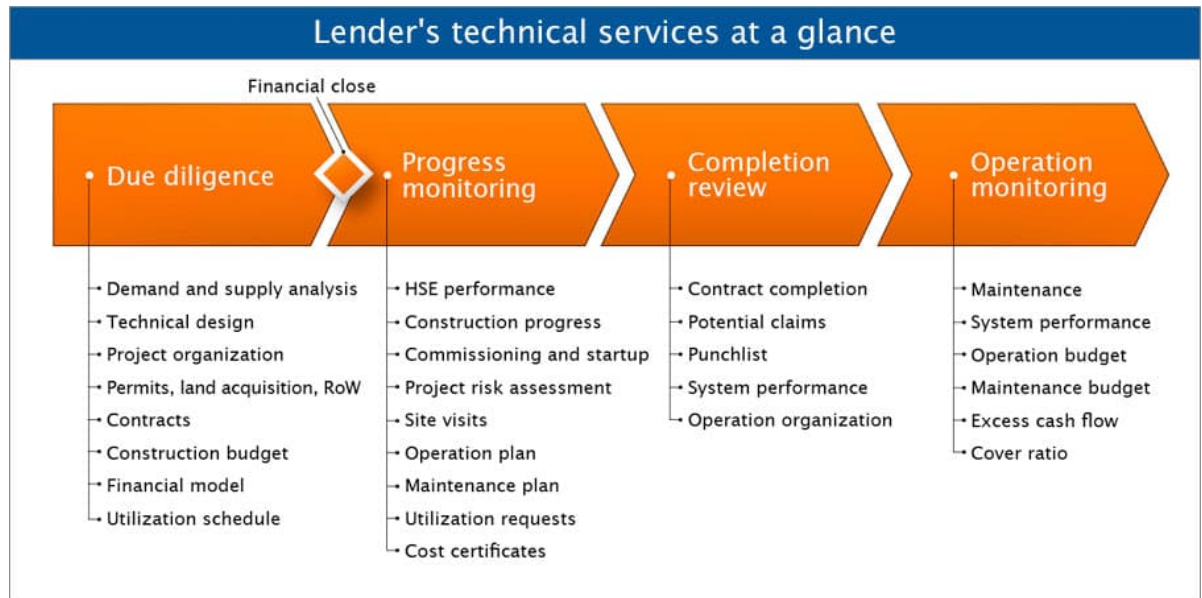


Figure 2: Technical Advisory Services.

ILF intends to perform the services in ILF-NGR Lagos Office. ILF will appoint a Project Manager, who shall be the primary point of contact with Client's project representatives. The Project Manager will be responsible for the entire project execution, coordination and completion in accordance with the scope of work requirements. This includes all management, contractual, commercial / financial, schedule and technical issues of the project.

Internal quality assurance reviews will be organized and performed by ILF's quality assurance Engineer in accordance with ILF's QA system. The QA Engineer advises the Project Manager for appropriate action in case of non-compliance with the established QA systems.

The Subject Matter Experts (SME) are fully responsible for their technical / commercial disciplines to comply with the scope of work, they report directly to the Project Manager. The Project Manager and the SMEs co-ordinate, organise and supervise the back-room discipline personnel who will provide review of documentation and analysis as required by the SMEs.

ILF Engineers Nigeria Ltd. intends to perform the Lender's Technical Advisory Services in order to achieve the following;

- To provide a review and assess function regarding the planning, monitoring, controlling and coordination activities of the project in achieving the project goal.

In the following description ILF will outline the methodological approach, working plan, work organization and resource staffing with key experts to execute the project according to formulated requirements. The offered services will be performed in close coordination and cooperation with the client.

6.2 EPC Contract

During this phase, the Technical Advisor (TA) shall carry out the following key activities;

- Review EPC Contractor planned execution methodology for practicability.
- Review contract approved vendors and subcontractor list in order to ensure that all aspects of the project scope have been considered and no identifiable conflicts, e.g Procurement, Shipment and Transportation to Site, Pipe Coating, Pipe lay, Non-Destructive Testing, Excavation and other Civil Works, etc.
- Review EPC Contractor project execution schedule for key installation parameters, e.g. procurement lead times, construction sequence etc.
- Confirm that the contract is in line with the specified contract type (FIDIC silver book) and that contract is fixed price, date certain.
 - o Comment on the adequacy of EPC packaging and reasonableness of contractual terms (e.g. work program, project cost, project delivery milestones and associated payment milestones/amounts, allocation of risks, performance guarantees/warranties and contingency provisions).
 - o Verify that the EPC contract has appropriate provisions for Liability Limits, Defects Liability Period(s), Liquidated Damages (LDs) and clear execution plan to meet specification and delivery time.
 - o Evaluate the potential for scope change or variation orders as well as implications and consequences on Project costs.
 - o Recommend specific action plan to mitigate any identified risks or conditions of the EPC contract.
- Review project delivery and payment milestones in line with industry standard practices and in addition, assess the adequacy of the EPC submission from the contractor.
- Assess the level of completeness of the EPC Contract documents and ensure provisions have been made to ensure project delivery in line with client objectives.
- Review EPC contractor inspection and test plans in order to ensure that at key hold points, EPC contractor has allowed for external/third party witnessing.

6.3 Engineering Design Review

Front End Engineering Design and Detailed Design are expected to be executed by the EPC Contractor. ILF assumes that the design work shall include the Inside Battery Limit (ISBL) and Outside Battery Limit (OSBL) of the facility.

ILF shall review each design stage appropriately, however, such review shall be done in milestones and not based on of available documentation. The following stages of review shall apply;

Front End Engineering Design

- Review of Basis of Design, process simulations, P&IDs, overall plant layouts and overall utility block diagrams (Electrical, Instrumentation, Communication etc ,
- Review of complete IFA packages based on agreed List of Deliverables

Detail Engineering Design

- Review IFR Packages based on agreed List of Deliverables
- Review IFA Packages / Procurement Packages based on agreed List of Deliverables
- Review IFC Packages / Procurement Packages based on agreed List of Deliverables

NOTE:

ILF shall treat the main process plant as a black box and verify only the expected inlet and outlet gas conditions.

ILF assumes that the design effort shall be robust and adequate to execute all aspects of the facility. The Consultant shall:

- Review contractor(s) Engineering Design activities; including design calculations, drawings, specifications, purchase orders, operating and maintenance manuals.
- Review Design/Engineering deliverables and to recommend to the client for approval.
- To provide professional advice to the client on design related issues.
- Lead and organize the safety review sessions such as HAZID, HAZOP and Constructability on all design deliverables. A third-party facilitator shall be provided via contract with Client for these reviews.

- Review the reports from activities including detailed surveys, detailed site investigations and other investigations necessary for the preparation of the detailed designs and drawings.
- Reviewing works and supporting activities during the surveys, site investigations and other investigations as necessary for the preparation of the detailed designs and drawings.
- Monthly Certification of technical progress for work done by the construction contractor(s) for inclusion in the monthly certificates or towards issuance of a milestone/job completion certificate.

6.4 Procurement Supervision

- To review vendor's procurement plans (Equipment and Material) and as well for the General Construction Contractor to ensure they are realistic and adequate.
- Review of Factory Acceptance Test (FAT) report and other vendor inspections, as well as vendor documentation for compliance with project requirements.
- Coordinate, attend and review Factory Acceptance Tests and Inspection of major Equipment and Materials carried out at Manufacturers and/or Suppliers sites for all major items of Equipment and Materials (where required) to ensure that all inspection and tests are carried out to the required level.
- To monitor delivery status of material and equipment to site based on the vendor's Procurement Plans.
- Issuance of regular procurement status reports to the client based on agreed frequency throughout the procurement phase of the project.
- Preparation of an integrated implementation schedule for the project.

6.5 Construction Monitoring

ILF shall monitor the construction activities and ensure adherence to construction execution plans with respect to planning, scheduling, progress measurement, reporting, and administrative services are being completed in a safe, efficient, and timely manner in accordance with the Project Contracts, Project HSE requirements, Project Budget and Project Schedule.

ILF shall carry out random checks and periodically request evidence with regard to being compliant with the applicable country's regulatory requirements. The obtaining of such permits is not the responsibility of ILF, but that of the Construction Contractor. Prior to the

signing of a Contract, the Construction Contractor shall provide to the Client in advance, evidence that they are qualified to operate and perform construction activities in Nigeria, throughout the Project execution period.

ILF shall monitor and ensure that the Construction Contractor provides all inspection and/or testing reports and other related documentation required during construction in accordance with Project Contract requirements.

ILF shall monitor the construction on site with respect to HSE, including, but not limited to:

- the organizing and implementing, safety and quality environmental awareness trainings for their workforce, as well as that of their subcontractors and suppliers, for the duration of the Project Work in accordance with the approved procedures; and
- The compliance with the Project HSE requirements with respect to the provision, transport, storage, conservation, operation, and maintenance of the construction equipment and tools.

ILF shall monitor compliance during construction on site with Project Contract requirements, with respect to quality assurance and quality management.

ILF shall develop for the Client's approval, the construction quality assurance requirements framework for the Project Work. ILF shall monitor but shall not be responsible for the Construction Contractor's material management and its being in accordance with the requirements contained in the Project Contracts. ILF shall inform the Client of any non-compliances, which are observed and monitor the remedying thereof.

ILF shall coordinate with the Client, the Client's participation in the Final Acceptance activities related to the Project Work and any inspections related thereto and connected with these activities.

Key tasks of the ILF shall include:

- Perform technical advisory work including periodic inspection of construction activities at site, review of construction progress reports and assessment of performance against agreed milestones.
- Certify achievement of milestones or work task prior to payment against relevant milestones.
- Review construction reports which set out, in reasonable detail, work carried out on the Project with commentary on likelihood of meeting the next milestone or any event which may delay the achievement, and issuance of monthly reports to the Client.
- Upon the request of Client, provide audits and reports to address specific queries.

- Review the construction schedule set out in the EPC Contract, compare with any revised schedules based on actual implementation.
- Provide to Client a description of any material disputes or proceedings (whether actual or threatened) relating to the Project during the previous month.
- Provide to Client a description of any accidents, emergencies or other events or circumstances which might have a material adverse impact on the construction schedule set out in the EPC Contract.
- Review and advise Client on any change orders or variations to the works under the Project Contracts and opine on the potential, or otherwise, for such variation to have a material impact on the Project.
- Obtain information on ongoing compliance with HSE/E&S requirements.
- Verify that required insurances are in place.
- Ensure that Client's covenants and conditions are being met where applicable.
- Review all relevant insurances required to be in place.
- Participate in, and report to Client on, all Project testing events (sectional and overall), including NMDPRA testing/certification programs.
- Review and signoff on the EPC Completion certificate.

6.6 Close-out Report

Prior to demobilizing of the TA, the team shall prepare a close-out report for the Client containing the following items:

- Diary of key events for the Project,
- Project status overview,
- Summary of outstanding work,
- Summary of key lessons learnt from Project implementation,
- Recommendations for further support,
- Operations handover status summary,
- Status of outstanding warranty items, and
- Operator execution plan for remainder of warranty period.



6.7 Location

ILF (The Consultant) will setup a dedicated office within ILF's existing facility in Lagos for the execution of the TA services (at no set-up cost). The Consultant's Project Management Team would be based in this office and coordinate the activities of the project from its Lagos office.

The Engineering Design Management and Vetting team would be based in this office as well and coordinate all engineering efforts of the EPC contractor(s).

Office space shall be provided in individual EPC Contractor's camp or site location.

6.8 Key Resources

Table 2 – Key resource

ID	Names	Role/Position
1	Obe Seyi	Project Manager
2	TBD	Project Engineer
3	Titilayo Giwa	Contracts Manager
4	QA / QC Engineer	Harrison Igbokweze
5	Willoughby Evelyn	Document Control Specialist
6	Gobir AbdulMuminu	Engineering Manager
7	Olusuji Ogungbangbe	Package Specialist
8	Yewande Akinrinmade	Lead Process Engineer
9	Olumide-George Dawodu	Senior Process Designer
10	Samson Amila	Lead Mechanical Engineer
11	TBD	Senior Mechanical Engineer
12	Opeola Afolabi	Lead Civil & Structural Engineer
13	Abdulfatai Ogunleke	Senior Civil & Structural Engineer
14	Badejo Rahmon	Lead Pipeline Engineer
15	Olaleye Olusina	Civil & Structural Designer
16	Christopher Ugwu	Lead Instrument & Control Engineer
17	Charles Benwari	Lead Electrical Engineer

Attachment 2 – Resume of key Personnel

6.8.1 Manning Chart

Service Items	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	MM / MW
Review of Existing Documents																					
Front End Engineering Design																					
Review of Basis of Design, P&IDs, Layouts, Block Diagrams																					
Review of IFA Packages																					
Detailed Engineering Design																					
Review IFR Packages																					
Review IFA Packages / Procurement Packages																					
Review IFC Packages / Procurement Packages																					
Procurement & Fabrication																					
Civil Construction																					
Site Presence (Every other week visit to site)																					
Shipping to Nigeria																					
Equipment Erection																					
Site Presence (Every other week visit to site)																					
Tank Farm Erection																					
Site Presence (Every other week visit to site)																					
Pipeline Installation																					
Site Presence (Every other week visit to site)																					
E&I Installation																					
Site Presence (Every other week visit to site)																					
Commissioning																					
Site Presence (Every other week visit to site)																					

Figure 3:Preliminary Execution Strategy .

Cat.	Name	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16
A	Project Manager	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10
A	Engineering Manager																
A	LNG Package Specialist	0.05	0.05	0.05	0.05												
A	Engineering Manager / Lead Process Engineer	0.20	0.20	0.20													
A	Lead Mechanical Engineer		0.10	0.10	0.10	0.10											
A	Lead Civil/Structural Engineer		0.20	0.20	0.10	0.10											
A	Lead Electrical Engineer			0.20	0.20	0.10											
A	Lead I&C Engineer			0.10	0.10	0.10											
B	Contracts Manager	0.05	0.05	0.05													
B	Senior Mechanical / Piping Engineer		0.20	0.20	0.20	0.20	0.05	0.05	0.05	0.05	0.05	0.05	0.05				
B	Lead Pipeline Engineer		0.20	0.20	0.20												
B	Senior Civil / Structural Engineer																
B	Senior Electrical Engineer						0.05	0.05	0.05	0.05	0.05	0.05	0.05				
B	Senior I&C Engineer						0.05	0.05	0.05	0.05	0.05	0.05	0.05				
C	Project Engineer	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20
C	QA/QC Engineer	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10	0.10
C	HSE Officer	0.05	0.05	0.05	0.05	0.05	0.05	0.05	0.05	0.05	0.05	0.05	0.05	0.05	0.05	0.05	0.05
C	Senior Process Engineer	0.20	0.20	0.20													
C	Civil/Structural Engineer		0.20	0.20	0.20	0.20											
C	Electrical Engineer			0.20	0.20	0.20											
C	I&C Engineer			0.20	0.20	0.20											
C	Civil & Structural Site Supervisor						0.50	0.25	0.50	0.25	0.25	0.25	0.25				
C	Mechanical & Piping Site Supervisor									0.25	0.50	0.25	0.50	0.25	0.50	0.25	0.25
C	Pipeline Site Supervisor													0.50	0.25	0.25	0.25
C	I&E Site Supervisor												0.25	0.25	0.50	0.25	0.50
D	Document Control Coordinator	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20	0.20
		1.15	2.05	2.75	2.20	1.85	1.30	1.05	1.30	1.30	1.55	1.30	1.80	1.65	1.90	1.40	1.65

Figure 4: Manning Chart.

6.9 Safety on Site

Safe and secure working conditions are an essential prerequisite for Consultant's activities on construction sites, camps and in the project area in general.

Should the situation or new discoveries or events on the ground provide reason for doubt concerning the security level on site or in country, Consultant reserves the right, in its own estimation and based on its own assessment, to suspend the affected part of the Services until doubt is cleared and an acceptable security level is re-established.

Client and Consultant will jointly ensure best efforts to establish confidence and share related information on the security level in a transparent and continuous manner.

7 COMMERCIAL PROPOSAL

ILF shall conduct the above scope of services under the following commercial terms consisting of monthly visit (one (1) trip of five days each in every month) to the site location on commencement of construction:

7.1 Labour Cost

		Labour Costs (USD)	Total (USD)
Offer	:	\$ 151,350.00	\$ 151,350.00

7.2 Non Labour Costs

		Non-Labour Costs (USD – Transport and Accommodation (excluding flights))	Total (USD)
Budget Offer	:	\$ 9,600.00	\$ 9,600.00

Note: Payment shall be made in Naira at the prevailing NAFEX exchange rate on the day of payment.

Notes:

- The above price is based on Scope of Work specified in this proposal and exclusive of VAT.
- The above price ensures that minimum manning levels are always available and can be increased as required based on project demands without recourse to additional sums within the contract duration.
- The above prices is limited to the number of and duration of site visits stated above. Additional site visits shall be reimbursed. The above prices do not contain any travel expenses and accommodation outside Nigeria.
- The above cost proposal is for information and budgeting purposes only. This service proposal is valid as a whole

- e) ILF expects that all Regulatory permits should have been secured by Client while EPC Contractor shall be responsible for all other permits/ licenses and as required for construction works.
- f) The price does not contain any cost for services to be provided by third party inspection services.
- g) Regular working time onsite during site surveys is 6 days per week, 10h per day; and
- h) Working time in Nigeria for Expat Staff is limited to 6 days per week, 10h per day.

7.3 Payment Schedule

Milestone	Description	Offer
Mobilisation	22.5% of Budget	\$36,213.75
Completion of FEED Review	7.5% of Budget	\$12,071.25
Completion of DED Review	10% of Budget	\$16,095.00
Submission of Report No. 7	Fixed Monthly Payment	\$9,657.00
Submission of Report No. 8	Fixed Monthly Payment	\$9,657.00
Submission of Report No. 9	Fixed Monthly Payment	\$9,657.00
Submission of Report No. 10	Fixed Monthly Payment	\$9,657.00
Submission of Report No. 11	Fixed Monthly Payment	\$9,657.00
Submission of Report No. 12	Fixed Monthly Payment	\$9,657.00
Submission of Report No. 13	Fixed Monthly Payment	\$9,657.00
Submission of Report No. 14	Fixed Monthly Payment	\$9,657.00
Submission of Report No. 15	Fixed Monthly Payment	\$9,657.00
Submission of Report No. 16	Fixed Monthly Payment	\$9,657.00

Table 3: Payment Schedule

7.4 Reimbursable Rates

The services to be rendered by the Consultant outside of the above scope of work and the execution proposal shall be on a reimbursable basis exclusive of VAT based on previously agreed rates and weekly approved timesheets. The table below shows ILF standard rates:

Cat.	Qualification	HOURLY RATES IN USD	
		ILF rates office works	ILF rates Works Nigeria
		Nigeria (Expatriates)	(Local staff)
A	Project Manager / Senior Consultant / Construction Manager / Engineering Manager / Lead Engineers	244	107
	Senior Engineers and Senior Construction Engineers	195	75
C	Engineers and Site Engineers	154	54
D	Technicians / Technical Draughtsman and qualified Assistance	124	49
E	Supporting Staff		40

Table 4: Reimbursable Rate

General Notes:

- ILF-Rates for 2026 are valid until December 31st, 2026.
- Above rates apply for ILF-employees, agency personnel and consultants managed by ILF.
- Rates includes general overheads, management, administration, office services, office rent, furniture and office equipment, drafting and secretarial supplies, computer hardware, general and normal engineering software, local communications, normal in-house reprographic services (including up to 3 copies of draft and 3 copies of final documents), insurance, payroll burden, personnel taxes, holiday time, general office maintenance and profit.
- Regular working time in ILF Nigerian offices is 5 days per week, 8h per day.
- Regular working time onsite during site surveys is 6 days per week, 10h per day.
- Working time in Nigeria for Expat Staff is limited to 6 days per week, 10h per day.
- Rates are exclusive of VAT, which is to be reimbursed additionally where applicable.

- h. Payment shall be made within ten (10) calendar days after submission of each invoice.

7.5 Non Labour Costs

For activities executed outside the scope of work defined herein, the non-labour costs such as travel, accommodation, messing, etc., if applicable, are to be invoiced at documented cost plus 15% mark-up.

This Service Proposal covers the license costs only for the following software: Operating system, Microsoft Word, Excel, PowerPoint, Outlook, AutoCAD, and the associated software listed herein.

If any special software is required, it will be acquired by ILF Engineers Nigeria at documented cost plus 15% mark-up or directly by client.



8 ASSUMPTIONS AND EXCLUSIONS

- ILF's proposal does not include the Topographical Surveys, Soil Investigation and any environmental study;
- Project and document language shall be English.
- All Client provided documentation is available at the project kick-off and upon request if any other is required, no idle time waiting for receipt of documents is included here;
- A qualified third party inspector for QA/QC activities is required for all testing and inspection services.
- All Client's provided documentation is in English language, no contingencies have been included in this proposal for translation. Translation of documents can be done upon request but it will be considered as a Variation Order to this Contract.
- Access to the Terminal is granted, no idle time is considered due to strikes, accessibility problems due to terminal operator's refusal to grant access, traffic conditions, local unrest, local communities, etc.;
- Safety, Health and Environment protection while ILF Team is at site falls under the Client Responsibility including safety induction prior accessing the site. No resources are considered in this proposal from ILF for such.
- Client shall provide third party inspection services for all quality inspections both at site and any fabrication locations. It is assumed that third party inspection (TPI) will be contracted directly by Client, in coordination and under the supervision of the Consultant.
- The expected review time for documents submitted to Client is 5 working days. No contingencies are included in this proposal for a longer review time.
- No procurement is envisaged and this priced proposal does not cover procurement. Any necessary procurement shall be approved by Client and made by ILF at cost plus 5%.
- Client shall be responsible for the development of the gas supply pipeline and all other supporting infrastructure. Technical Advisory services related to these are not included in the current scope.

8.1 Exclusions from Services

Please accept the following exclusions from our Services:

- Purchase / supply of any equipment;
- Any kind of procurement activities or procurement documents;
- Any costs of the Company, licensors, authorities or third parties (incl. endorsement of documentation, personnel costs and applicable fees for permits, etc.) as well as their travel expenses and allowances;
- Authority engineering;
- Costs arising from participation of a third party are excluded from our services. Such costs are based on national principles and cannot be estimated yet (e.g. certified bodies, etc.);
- Supply of any equipment (exempted from this are those facilities which are necessary for carrying out the services);
- Local fees and charges that may be associated with the execution of the work on site;
- Adaption of existing documentation in case of missing or incorrect data, conversion of the existing documentation into editable files (e.g. AutoCAD).
- Any travel costs for Company's personnel (e.g. visas, tickets, accommodation, meals, daily allowance, insurance, etc.)

9 CONTRACT

Consultant proposes a FIDIC Client/Consultant Services Agreement as the Form of Agreement for the Project. The following sections include proposed major terms to be included in the Particular Conditions clauses.

9.1 Contractual Liability Cap

The Consultant would like to propose to cap the total aggregate of the contractual liability to a maximum value of 30% of the received remuneration on the Project.

9.2 Project Language

The Consultant proposes that the Project language is English.

9.3 Exclusion of Consequential Damages

The Consultant proposes exclusion of the consequential damages related to the Project. No compensation shall be payable by Consultant for indirect and/or consequential damage and loss of profit of the Client. This will be mutual for ILF and the Client



10 CONCLUSION

We trust that our above proposal meets the Client's approval. We remain at the Client's disposal in case that any further information or clarifications are required. We are looking forward to an opportunity to work with you on this Project.

Abiodun Oshodi

Managing Director

ILF Engineers Nigeria Ltd.



11 ATTACHMENTS

Attachment 1 – Company Brochures

Attachment 2 – Resume of key Personnel

